


GRAVELINE BAY MARSH CREATION PROJECT CONSTRUCTION UPDATE

JANUARY 2023




- Contractor's dredge was out-of-service for 6 weeks. Construction recommenced in October 2022. Dredge breakdowns have slowed production.
- 47 of the 55 mounds have been created to date (1/31/2023).
- The mounds will be planted once they are all constructed. Oyster shell will be placed on the northern large mound.
- The contractor has received a change order for 90 more days to finish the project in May 2023.

PROGRESS MAP

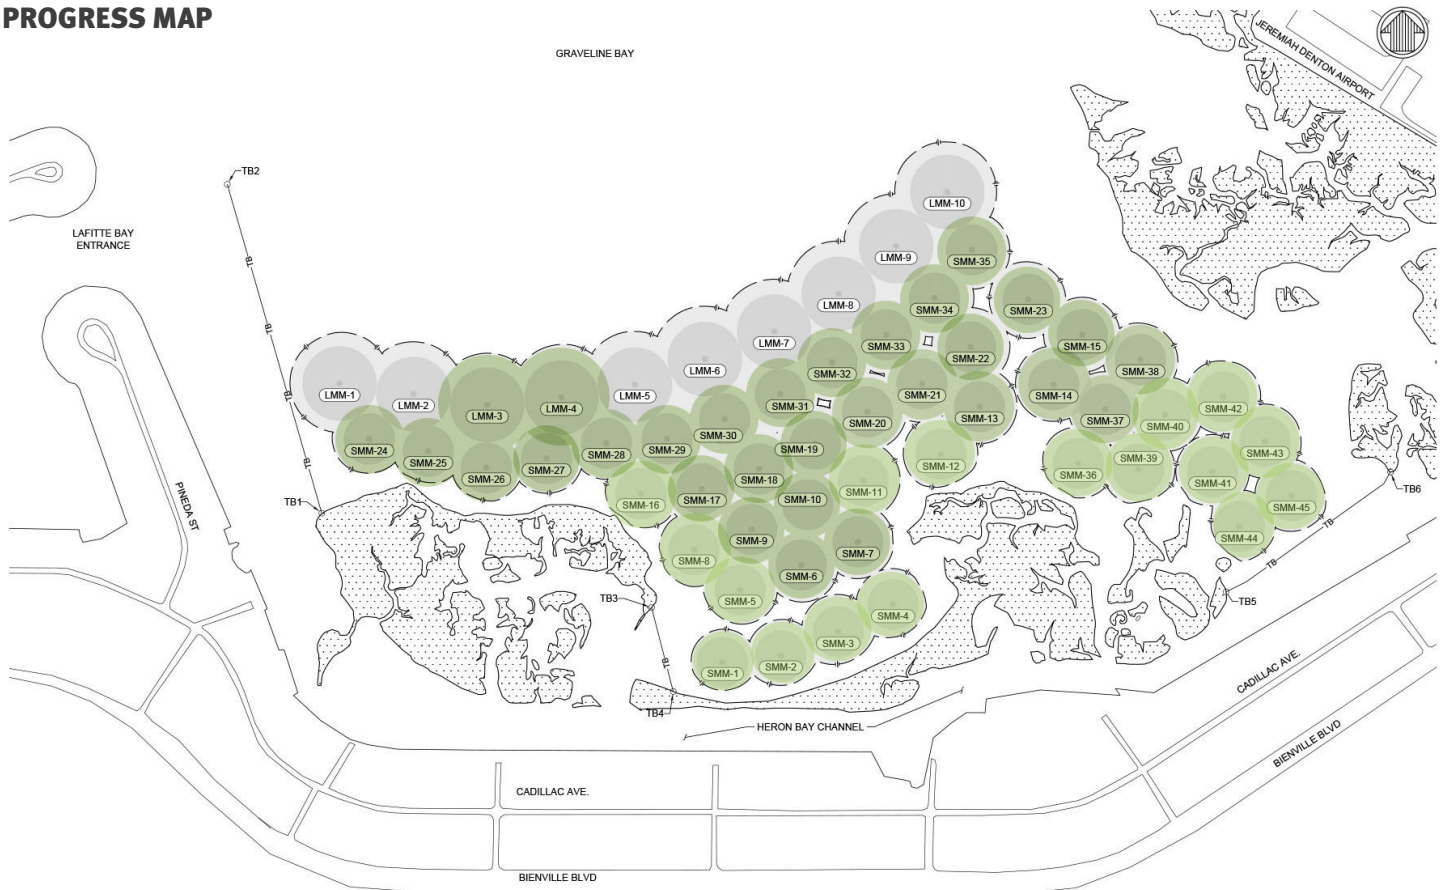

TIMELINE



Contact: Town of
Dauphin Island,
1011 Bienville
Blvd, Dauphin
Island, AL 36528 |
Tel: 251-861-5525
