

GRAVELINE BAY MARSH CREATION PROJECT CONSTRUCTION UPDATE




FEBRUARY 2023




- The last of the mounds are being finalized the first few weeks of March 2023.
- The mounds will be planted in late March, early April in time for the growing season.
- Oyster shell will be placed on the northern large mound.
- Turbidity curtains will be removed as soon as the last marsh mound is finalized.
- The contractor has received a change order for 90 more days to finish the project in May 2023.

PROGRESS MAP

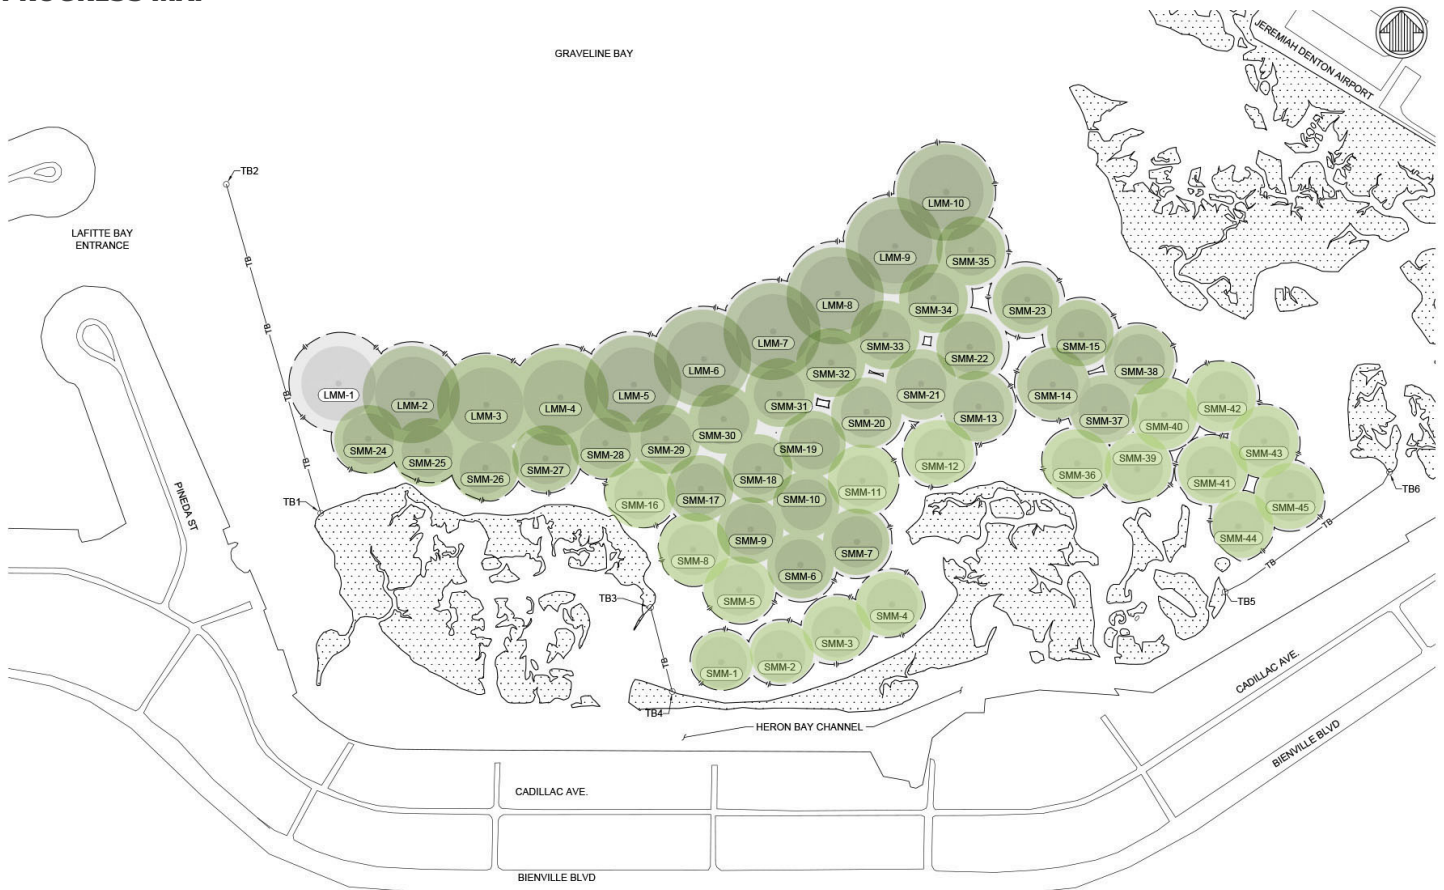

TIMELINE

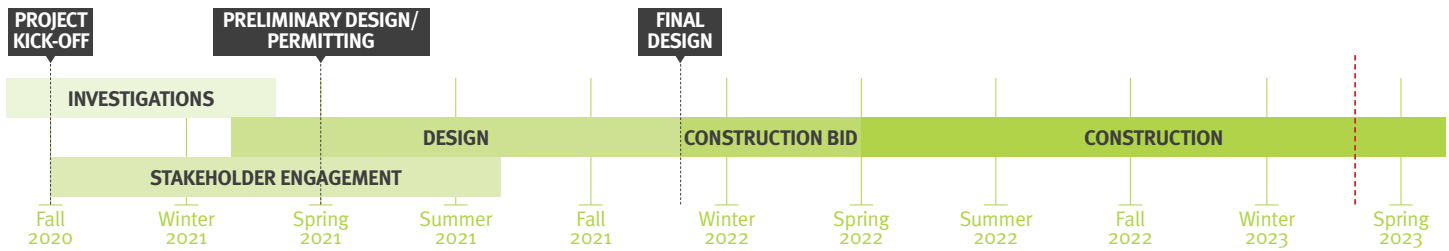

Contact: Town of Dauphin Island,
1011 Bienville Blvd, Dauphin Island, AL 36528 |
Tel: 251-861-5525
